

Headquarters Complex at Plant No. 1

Project No. P1-128A

Presented by:
Mike Dorman
Acting Director
of Engineering

Operations
Committee
May 3, 2023

Quarterly Update



1

Project Site




Headquarters
Complex

Administration
Building

2

2

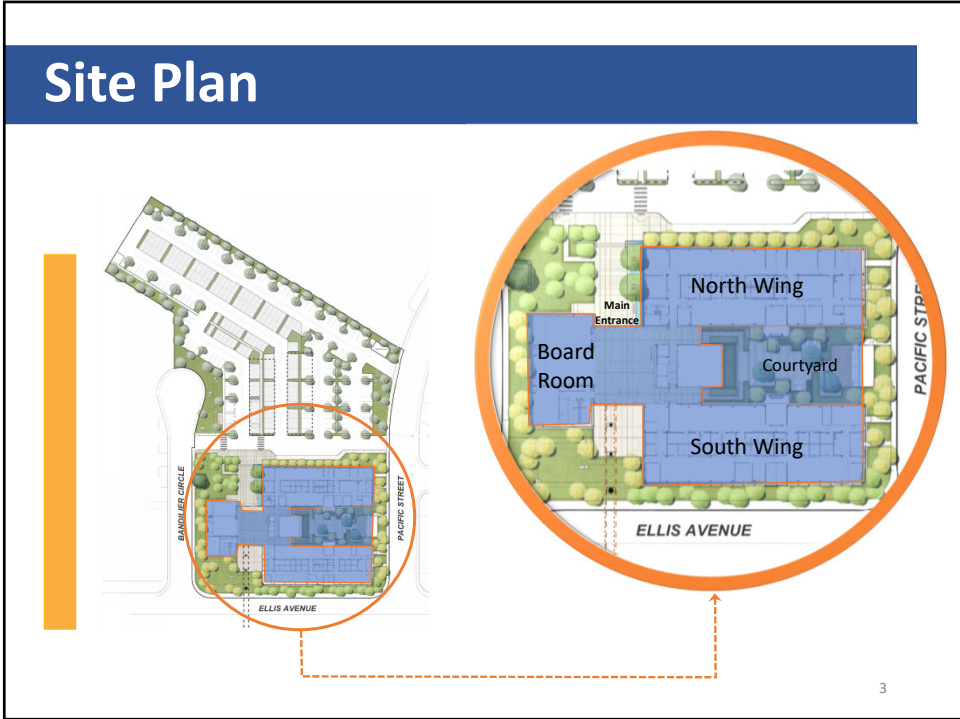

3



4

Lobby Entrance



5

5

Employee Workspace



Chilled Beam

Office/Open Workstation Area

6

6

Last Update and Now



7

7

Since Last Update

- Bridge foundation work at Plant No. 1 commenced
- Curtain wall install – window panels
- Building 5 demolition
- Roof work
- HVAC



8

8

Upcoming Activities

- Interior and exterior framing ongoing
- Begin bridge construction



Pedestrian sky bridge over Ellis Avenue connects to Plant No. 1

9

9

Other Procurement Status

Activity	Complete	Comments
IT network equipment procurement	✓	Dec 2022 Admin
Move management consultant hired	✓	Dec 2022 Admin
Furnishings, fixtures and equipment purchase order contract awarded	✓	April 2023 Ops
Audiovisual equipment bidding	✓	May 2023 Ops
Audiovisual installation procurement		July 2023 Ops

10

10

Project Status

Budget

Original Approved Contract	\$102,544,973	
6 Approved Change Orders	\$1,086,209	(\$4,041,040 Remaining)
Total Current Approved Contract	\$103,768,307	
Amount Invoiced	\$61,822,976	(60% of Total)

Schedule

- 72% of contract elapsed
- Final Completion: December 4, 2023 (contract)

11

11

Live Camera Feed

www.ocsan.gov/Headquarters


One-time registration to view camera footage

The screenshot shows the OCSAN website interface for the 'Headquarters Administration Building Project'. The page includes a navigation menu, a search bar, and a 'More Information' sidebar. The 'Live Camera Feed' section is circled in red, indicating the registration process for viewing the camera footage.

12

12

Questions

A blue circle containing a white question mark is centered on the page. To the right of the circle is a vertical orange bar. The entire content is enclosed in a black rectangular border.
