



ORANGE COUNTY SANITATION DISTRICT
Capital Improvement Program
Contract Performance Report
For the period ending March 31, 2020

DATE: May 6, 2020

TO: Orange County Sanitation District
Board of Directors

FROM: James D. Herberg, General Manager
Through: Kathy Millea, Director of Engineering

This report summarizes the status, activities, and performance of public works construction contracts and consultant agreements. This report also identifies the names and status of projects being performed under master budgets for planning studies, research, small construction projects, O&M capital projects, and information technology projects.

Table of Contents

<u>Part 1 – Construction Contracts</u>	page 2
Active Construction Contracts	
Construction Contracts Closed in Last Quarter	
Cumulative Change Order Rates – Closed Construction Contracts	
<u>Part 2 – Engineering Services Agreements</u>	page 6
Active Engineering Services Agreements	
Active Task Orders by Master Agreement	
<u>Part 3 - Master Budget Projects</u>	page 10
Planning Studies Status Report	
Research Program Status Report	
Small Construction Projects Program Status Report	
Information Technology Capital Program Status Report	
Operations and Maintenance Capital Program Status Report	
<u>Part 4 - Supplemental Engineering Services Contract</u>	page 16
Supplemental Engineering Services Contract Status	
Supplemental Engineering Services Contract Labor Summary	




ORANGE COUNTY SANITATION DISTRICT Capital Improvement Program Contract Performance Report

For the period ending March 31, 2020

PART 1 - CONSTRUCTION CONTRACTS

Table 1 lists the construction contracts active as of March 31, 2020. The graph below shows the number and total value of projects broken down plant and collections.

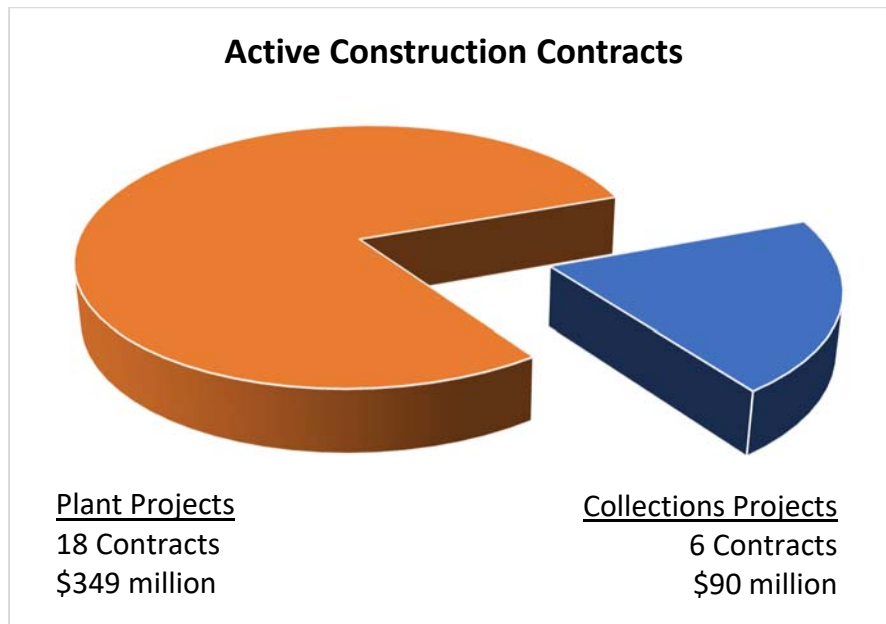

One construction contract was closed in this quarter, as listed in Table 2.

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020**

Table 1 - Active Construction Contracts

Project / Contract	Contractor	Award Date	Board Award Amount	Change Orders	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
2-41-8 SARI Rock Stabilizers Removal									
2-41-8 SARI Rock Stabilizers Removal	Griffith Company	09/26/2018	\$2,809,082	\$0	\$2,809,082	10.0%	10.0%	0.0%	10.0%
2-72 Newhope-Placentia Trunk Replacement									
2-72B Newhope-Placentia Trunk Replacement, Segment B	OHL USA, INC.	06/15/2018	\$58,242,000	\$533,357	\$58,775,357	6.5%	6.5%	0.9%	5.6%
3-62 Westminster Blvd Force Main Replacement									
3-62			\$27,743,000	\$0	\$27,743,000	10.0%	10.0%	0.0%	10.0%
J-117 Ocean Outfall System Rehabilitation									
J-117B Outfall Low Flow Pump Station	Shimmick Construction Co., Inc.	12/19/2018	\$90,200,000	\$105,983	\$90,305,983	8.0%	8.0%	0.1%	7.9%
J-126 Safety Improvements Program									
J-126C NFPA 820 HVAC and Electrical Improvements	MMC, Inc.	03/05/2019	\$469,000	\$0	\$469,000	10.0%	10.0%	0.0%	10.0%
J-126JK Stairs, Hatches, Walkway Hazards, Ladders, Guardrails, Roof Fall Protection	Olsson Construction, Inc.	10/24/2018	\$3,637,601	\$917	\$3,638,518	10.0%	10.0%	0.0%	10.0%
J-126PQ Ladders, Hatches, Roof Fall Protection	Tharsos Construction	11/28/2018	\$786,000	\$0	\$786,000	10.0%	10.0%	0.0%	10.0%
M-FE Small Construction Projects Program									
FE16-06 Fuel Cell Facilities Demolition	MMC, Inc.	07/24/2019	\$474,000	\$0	\$474,000	10.0%	10.0%	0.0%	10.0%
FE17-01 Carbon Canyon Pipeline Sag Repairs	Mike Pritch and Sons, Inc.	10/02/2019	\$510,000	\$0	\$510,000	10.0%	10.0%	0.0%	10.0%
FE17-05 Plant 1 ICS Network Extension	RP Controls	06/26/2019	\$321,889	\$0	\$321,889	10.0%	10.0%	0.0%	10.0%
FE18-18 Portable Generator Connector at Lido Pump Station	M. Brey Electric, Inc.	09/17/2019	\$42,285	\$0	\$42,285	20.0%	20.0%	0.0%	20.0%
M-FR Operationally-Funded Projects									
FE17-06 Tustin Ave Manhole and Pipe Repair	Nuline Technologies, LLC	10/24/2019	\$350,000	\$0	\$350,000	10.0%	10.0%	0.0%	10.0%
MP-248 P2 Secondary Clarifier Repairs (AS Plant)	W. M. Lyles Company	06/26/2019	\$3,048,000	\$0	\$3,048,000	10.0%	10.0%	0.0%	10.0%
MP-105 P2 CENGEN Steam Turbine Rehabilitation	Dresser-Rand	03/25/2018	\$245,424	\$0	\$245,424	20.0%	20.0%	0.0%	20.0%
MP-509 P2 Headworks Low Voltage Cable Assessment	Mass Electric Construction Co.	12/18/2019	\$434,327	\$0	\$434,327	20.0%	20.0%	0.0%	20.0%
MP-638 Activated Sludge Plant Clarifier Inlet Gate Replacement at Plant No. 2	Innovative Construction Solutions	12/18/2019	\$658,300	\$0	\$658,300	10.0%	10.0%	0.0%	10.0%
P1-101 Sludge Dewatering and Odor Control at Plant 1									
P1-101 Sludge Dewatering and Odor Control at Plant 1	WM Lyles Company	11/28/2012	\$126,908,300	\$12,785,479	\$139,693,779	3.0%	11.5%	10.1%	1.4%
P1-115 Title 24 Access Compliance and Building Rehabilitation Project									
P1-115B Rehabilitation of Fleet Services Building, Building 8 and Paving Area	ODC Engineering & Technology	09/11/2017	\$2,235,563	\$61,194	\$2,296,757	10.0%	10.0%	2.7%	7.3%
P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1									
P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1	Abhe & Svoboda, Inc.	07/24/2019	\$6,863,092	\$0	\$6,863,092	10.0%	10.0%	0.0%	10.0%
P2-110 Consolidated Demolition and Utility Improvements at Plant 2									
P2-110 Consolidated Demolition and Utility Improvements at Plant 2	Flatiron West Inc	02/09/2017	\$16,730,000	\$1,446,982	\$18,176,982	8.0%	13.0%	8.6%	4.4%
P2-122 Headworks Modifications at Plant No. 2 for GWRS Final Expansion									
P2-122 Headworks Modifications at Plant No. 2 for GWRS Final Expansion	Shimmick Construction Co., Inc.	01/22/2020	\$14,487,735	\$0	\$14,487,735	10.0%	10.0%	0.0%	10.0%
P2-123 Return Activated Sludge Piping Replacement at Plant 2									
P2-123 Return Activated Sludge Piping Replacement at Plant 2	Shimmick Construction Co., Inc.	09/25/2019	\$6,042,110	\$0	\$6,042,110	10.0%	10.0%	0.0%	10.0%
P2-92 Sludge Dewatering and Odor Control at Plant 2									
P2-92 Sludge Dewatering and Odor Control at Plant 2	Shimmick Construction Co., Inc.	01/12/2015	\$49,850,000	\$2,030,417	\$51,880,417	5.0%	6.0%	4.1%	1.9%
P2-98 Primary Treatment Rehabilitation at Plant No. 2									
P2-98B B/C-Side Primary Clarifiers Interim Repair at Plant 2	Myers & Sons Construction, LLC	01/23/2019	\$8,665,000	\$30,920	\$8,695,920	10.0%	10.0%	0.4%	9.6%
Total			\$421,752,708	\$16,995,249	\$438,747,957				

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020**

Table 2 - Construction Contracts Closed in Last Quarter


Project / Contract	Contractor	Date Closed	Award Date	Board Award Amount	Change Orders	Final Contract Amount	Original Contingency	Current Contingency	Contingency Used	Unused Contingency
J-117 Ocean Outfall System Rehabilitation										
J-117A Interplant Effluent Pipeline Rehabilitation	Shimmick Construction Co., Inc.	01/07/2020	08/07/2017	\$12,609,012	\$980,224	\$13,244,050	8.0%	8.0%	7.8%	0.2%
J-126 Safety Improvements Program										
J-126L Various	IQA Construction	02/18/2020	06/06/2018	\$212,700	\$19,933	\$232,000	10.0%	10.0%	9.4%	0.6%
M-FE Small Construction Projects Program										
FE14-05 Plant No. 1 Fleet Services UST Leak Remediation	Engineering/Remediation Resources Group, Inc.	03/31/2020	01/23/2019	\$648,675	\$26,085	\$674,760	20.0%	20.0%	4.0%	16.0%
FE15-07 Secondary Treatment and Plant Water VFD Replacement at Plant 1	Helix Electric	03/17/2020	03/28/2018	\$1,797,000	\$90,543	\$1,879,440	10.0%	10.0%	5.0%	5.0%
Total				\$15,267,387	\$1,116,785	\$16,030,250				



ORANGE COUNTY SANITATION DISTRICT Capital Improvement Program Contract Performance Report

For the period ending March 31, 2020

When the Sanitation District Board awards a construction contract, they also approve a contingency which allows the General Manager to approve contract change orders up to the amount of the contingency. One purpose of this report is to document how much of the contingency is utilized. A contract's change order rate is only meaningful when the work is completed. As such, the change order performance charts in this report are based only on contracts closed since the Board began approving contingencies in 2008. The following chart shows how cumulative change order rates have changed for plant, collections, and all contracts since the contingency system was implemented.

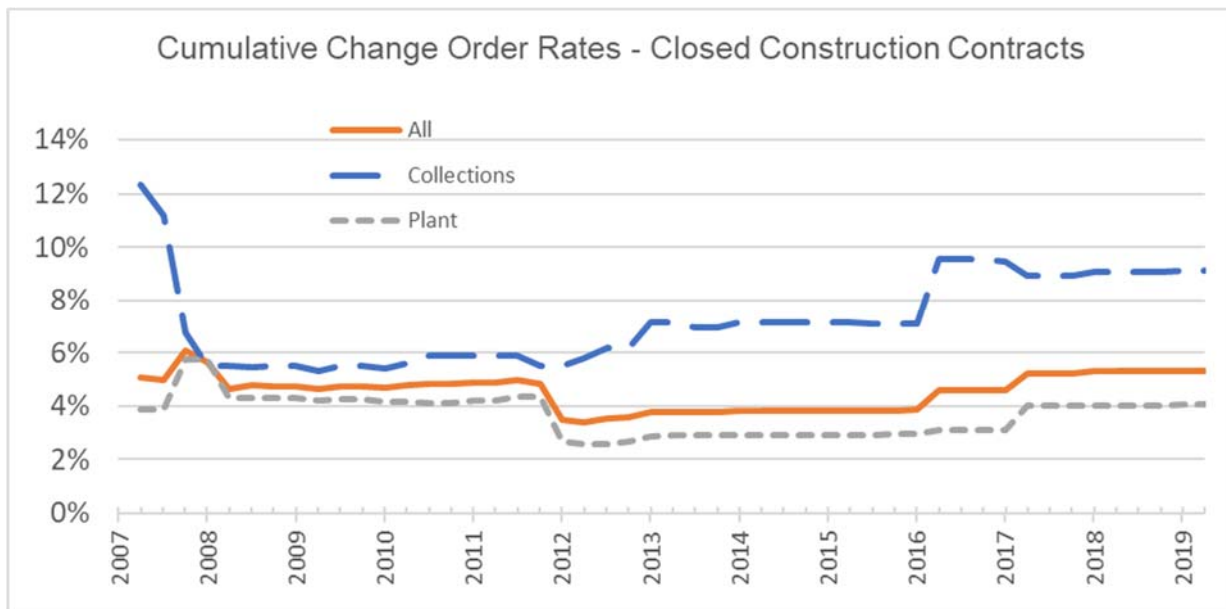



ORANGE COUNTY SANITATION DISTRICT

Capital Improvement Program

Contract Performance Report

For the period ending March 31, 2020

PART 2 – ENGINEERING SERVICES AGREEMENTS

The Sanitation District engages engineering consultants through Professional Service Agreements (PSAs), Professional Design Services Agreements (PDSAs), Professional Construction Services Agreements (PCSAs), and Master Professional Services Agreements (Master Agreements). PDSAs are used to obtain design engineering services, and PCSAs are a subsequent agreement with the design consultant to provide support services during construction. PSAs are used for planning studies and other consultant assignments.

Master Agreements are issued to a pool of pre-qualified consultants for smaller projects. On those smaller projects, the Sanitation District solicits task order proposals from three or four of the firms and awards a task order to the most qualified consultant. There are currently six sets of Master Agreements.

- 2012 Master Design Agreements (expired)
- 2015 Master Design Agreements (expired)
- 2018 Master Design Agreements
- 2017 Master Agreements for CEQA Studies
- 2017 Master Agreements for Collection Planning Studies
- 2017 Master Agreements for Wastewater Treatment Planning Studies

The two Master Design Agreements from 2012, and 2015 have expired, meaning no new task orders can be issued under them, but previously-issued task orders remain active until completed. Task Orders are limited by Sanitation District Ordinance No. OCSD-52 \$300,000 per task order.

A status table for all Active Engineering Services Agreements (PDSAs and PCSAs) is attached under Table 3, and a status table for all Active Task Orders by Master Agreement is attached under Table 4 (Master Agreements).

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020**

Table 3 - Active Engineering Services Agreements

Project / Contract	Type	Consultant	Award Date	Board Award Amount	Amendments	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
2-41-8 SARI Rock Stabilizers Removal										
2-41-8 SARI Rock Stabilizers Removal	PCSA	Michael Baker International, Inc.	09/26/2018	\$215,129	\$0	\$215,129	10.0%	10.0%	0.0%	10.0%
2-72 Newhope-Placentia Trunk Replacement										
2-72 Newhope-Placentia Trunk Replacement	PCSA	Lee & Ro	03/23/2016	\$3,253,946	\$0	\$3,253,946	10.0%	10.0%	0.0%	10.0%
2-72 Newhope-Placentia Trunk Replacement	PDSA	Lee & Ro	10/22/2014	\$8,468,232	\$434,974	\$8,903,206	10.0%	10.0%	5.1%	4.9%
3-62 Westminster Blvd Force Main Replacement										
3-62 Westminster Blvd Force Main Replacement	PCSA	Stantec Consulting Services, Inc.	12/18/2019	\$1,183,000	\$0	\$1,183,000	10.0%	10.0%	0.0%	10.0%
3-62 Westminster Blvd Force Main Replacement	PDSA	Stantec Consulting Services, Inc.	07/22/2015	\$6,917,175	-\$1,339,457	\$5,577,718	10.0%	10.0%	0.0%	10.0%
3-64 Rehabilitation of Western Regional Sewers										
3-64 Rehabilitation of Western Regional Sewers	PDSA	AECOM Technical Services, Inc.	01/27/2016	\$17,639,250	\$1,088,654	\$18,727,904	10.0%	10.0%	6.2%	3.8%
3-67 Seal Beach Pump Station Replacement										
3-67 Seal Beach Pump Station Replacement	PDSA	Lee & Ro	11/20/2019	\$5,947,850	\$0	\$5,947,850	10.0%	10.0%	0.0%	10.0%
5-60 Newport Force Main Rehabilitation										
5-60 Newport Force Main Rehabilitation	PCSA	Brown and Caldwell	04/29/2014	\$2,231,925	\$839,714	\$3,071,639	8.0%	38.7%	37.6%	1.0%
5-67 Bay Bridge Pump Station Replacement										
5-67 Bay Bridge Pump Station Replacement	PDSA	Arcadis US Inc.	10/25/2017	\$7,137,000	\$368,955	\$7,505,955	10.0%	10.0%	5.2%	4.8%
6-17 District 6 Trunk Sewer Relief										
6-17 District 6 Trunk Sewer Relief	PCSA	RMC Water & Environment	10/10/2016	\$290,000	\$0	\$290,000	15.0%	15.0%	0.0%	15.0%
7-66 Sunflower and Red Hill Interceptor Repairs										
7-66 Sunflower and Red Hill Interceptor Repairs	PDSA	GHD	09/25/2019	\$308,712	\$0	\$308,712	10.0%	10.0%	0.0%	10.0%
J-117 Ocean Outfall System Rehabilitation										
J-117A Interplant Effluent Pipeline Rehabilitation	PCSA	Brown and Caldwell	05/24/2018	\$1,121,666	\$112,167	\$1,233,833	10.0%	10.0%	10.0%	0.0%
J-117B Outfall Low Flow Pump Station	PCSA	Brown and Caldwell	12/19/2018	\$8,563,913	\$0	\$8,563,913	10.0%	10.0%	0.0%	10.0%
J-124 Digester Gas Facilities Rehabilitation										
J-124 Digester Gas Facilities Rehabilitation	PDSA	Brown and Caldwell	11/15/2017	\$11,770,000	\$50,000	\$11,820,000	10.0%	10.0%	0.4%	9.6%
J-126 Safety Improvements Program										
J-126 Safety Improvements Program	PDSA	Arcadis	08/29/2016	\$3,040,000**	\$0	\$3,040,000	10.0%	5.1%	0.0%	5.1%
J-128 Project Management Information System										
J-128 Project Management Information System	Other	PMWeb, Inc.	05/24/2017	\$1,022,500	\$79,525	\$1,102,025	20.0%	20.0%	7.8%	12.2%
J-98 Electrical Power Distribution System Improvements										
J-98 Electrical Power Distribution System Improvements	PDSA	Brown and Caldwell	01/29/2020	\$2,240,000	\$0	\$2,240,000	10.0%	10.0%	0.0%	10.0%
M-FE Small Construction Projects Program										
FE16-11 Lane Channel Crossing	PSA	HDR Engineering, Inc.	06/28/2017	\$131,939	\$0	\$131,939	10.0%	10.0%	0.0%	10.0%
M-RESEAR Research Program										
RE17-02 Biogas Scrubber Evaluation	PSA	Carollo Engineers, Inc.	04/21/2017	\$656,783	\$63,097	\$719,880	15.0%	15.0%	9.6%	5.4%
M-STUDIE Planning Studies Program										
PS15-02 Edinger Pump Station Rehabilitation Study	PSA	Lockwood, Andrews & Newman, Inc.	12/20/2017	\$505,042	\$0	\$505,042	10.0%	10.0%	0.0%	10.0%
PS15-06 Seismic Evaluation of Structures at Plant Nos. 1 and 2	PSA	Geosyntec Consultants, Inc.	06/28/2017	\$2,578,028	\$132,425	\$2,710,453	10.0%	10.0%	5.1%	4.9%
PS15-08 Collections Capacity Evaluation Study	PSA	RMC Water & Environment	08/24/2016	\$2,802,675	\$19,372	\$2,822,047	10.0%	10.0%	0.7%	9.3%
PS16-01 Stormwater Master Plan	PSA	Michael Baker International, Inc.	07/26/2017	\$715,300	\$54,839	\$770,139	10.0%	10.0%	7.7%	2.3%
PS17-03 Active Fault Location Study at Plant No. 2	PSA	Letts Consultants International, Inc.	03/06/2019	\$868,286	\$0	\$868,286	10.0%	10.0%	0.0%	10.0%
PS17-08 CEQA - Facilities Master Plan	PSA	Dudek	02/27/2019	\$812,709	\$0	\$812,709	10.0%	10.0%	0.0%	10.0%
PS18-09 Ocean Outfall Condition Assessment and Scoping Study	PSA	Carollo Engineers, Inc.	03/25/2020	\$2,744,000	\$0	\$2,744,000	10.0%	10.0%	0.0%	10.0%
P1-101 Sludge Dewatering and Odor Control at Plant 1										
P1-101 Sludge Dewatering and Odor Control at Plant 1	PCSA	HDR Engineering, Inc.	06/28/2012	\$7,140,000	\$2,453,653	\$9,593,653	8.0%	35.0%	34.4%	0.6%
P1-105 Headworks Rehabilitation at Plant 1										
P1-105 Headworks Rehabilitation at Plant 1	PDSA	Carollo Engineers, Inc.	05/27/2015	\$17,528,957	\$7,710,955	\$25,239,912	10.0%	51.0%	44.0%	7.0%
P1-128 Headquarters Complex										
P1-128 Headquarters Complex	PDSA	HDR Engineering, Inc.	06/22/2016	\$11,785,709	-\$752,553	\$11,033,156	10.0%	10.0%	0.0%	10.0%
P1-128 Headquarters Complex	PSA	LSA Associates, Inc.	08/11/2016	\$420,927	\$0	\$420,927	10.0%	10.0%	0.0%	10.0%
P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1										

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020**

Table 4 - Active Task Orders by Master Agreement

Master Agreement / Project	Consultant	Award Date	Original Task Order Value	Amendments	Current Task Order Value	
2012 Master Professional Design Service Agreements (Expired)						
FE10-21 Area 02 Craig Regional Park Manhole Improvements	GHD	10/8/2012	\$58,440	\$41,560	\$100,000	
2015 Master Professional Design Service Agreements (Expired)						
FE14-05 Plant No. 1 Fleet Services UST Leak Remediation	Dudek	9/1/2015	\$86,116	\$73,137	\$159,253	
PS17-02 Guidelines for Development in the Area of OCSF Facilities	AECOM	8/21/2017	\$93,187	\$0	\$93,187	
2017 Master Agreements for Wastewater Treatment Planning Studies						
P1-101 Spill Prevention, Control, and Countermeasure Plan for Sludge Dewatering and Odor Control at Plant No. 1	AECOM	06/27/2018	\$28,216	\$10,935	\$39,151	
PS18-10 Root Cause Analysis of Malfunctioning Process Units at TFSC Facility at Plant No. 2	Brown and Caldwell	2/6/2019	\$24,783	\$0	\$24,783	
PS18-01 Asset Management Plan Development	HDR Engineering, Inc.	04/03/2019	\$274,777	\$0	\$274,777	
PS17-10 Emergency Overflow Weirs, Wing Wall Structural and Geotechnical Investigations	HDR Engineering, Inc.	05/21/2019	\$260,415	\$0	\$260,415	
PS18-05 Plant No. 2 Future Site Plan Development	Brown and Caldwell	05/22/2019	\$122,389	\$0	\$122,389	
PS18-11 ETAP Model Updates for Plant Nos 1 and 2	Brown and Caldwell	3/17/2020	\$227,412	\$0	\$227,412	
2017 Master Agreements for Collection Planning Studies						
No Task Orders Issued to Date	--	--	--	--	--	
2017 Master Agreements for CEQA Studies						
No Task Orders Issued to Date	--	--	--	--	--	
2018 Master Professional Design Service Agreements						
J-127 Natural Gas Pipelines Replacement at Plant Nos. 1 and 2	Black & Veatch	1/21/2019	\$271,964	\$0	\$271,964	
FE18-19 12KV Distribution Center B and East RAS Pump Station Roof Replacement	HDR Engineering, Inc.	09/16/2019	\$74,771	\$0	\$74,771	
FE18-15 Plant Boiler System Relief at Plant No. 2	IDS Group, Inc.	10/22/2019	\$23,299	\$0	\$23,299	
FR2-0013 Trickling Filter Sludge Pump Room Exhaust Fan Relocation at Plant No. 2	AECOM	11/6/2019	\$75,120	\$0	\$75,120	
FE18-14 Plant Water Pipeline Replacement in Kinnison, Lindstrom, and Scott Tunnels at Plant No. 2	Dudek	11/6/2019	\$108,308	\$0	\$108,308	
FE18-16 Truck Loading Basement Drain Modifications at Plant No. 1	GHD, Inc.	12/4/2019	\$70,130	\$0	\$70,130	
P1-135 Digester Ferric Chloride Piping Replacement at Plant No. 1	Dudek	2/19/2020	\$127,174	\$0	\$127,174	
FE18-13 Redhill Relief Sewer Relocation at State Route 55	GHD, Inc.	3/27/2020	\$168,612	\$0	\$168,612	
			Total	\$2,095,113	\$125,632	\$2,220,745



ORANGE COUNTY SANITATION DISTRICT
Capital Improvement Program
Contract Performance Report
For the period ending March 31, 2020

PART 3 – MASTER BUDGET PROJECTS

The Board-adopted budget for Fiscal Years 2018-19 and 2019-20 includes master program budgets that allow staff to more quickly initiate, execute, and manage smaller projects that fit within the scope of a particular program. The projects chartered under these program budgets are referred to as sub-projects and are managed to the same standards as projects specifically listed in the adopted budget. A status table for each of these programs listing the sub-projects is attached.

Master Program Title	Status Table
Planning Studies Program	Table 5
Research Program	Table 6
Small Construction Projects Program	Table 7
Information Technology Capital Program	Table 8
Operations & Maintenance Capital Program	Table 9

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020
Table 5 - Planning Studies Status Report**

Project Number	Project Name	Status	Allocated Budget
PS15-02	Edinger Pump Station Rehabilitation Study	Active	\$ 971,000
PS15-06	Seismic Evaluation of Structures at Plant Nos. 1 and 2	Active	\$ 3,860,000
PS15-08	Collections Capacity Evaluation Study	Active	\$ 3,682,000
PS15-10	2017 Facilities Master Plan	Active	\$ 3,850,000
PS16-01	Stormwater Master Plan	Active	\$ 1,415,700
PS16-02	SCE Feed Reliability Improvements Study	Active	\$ 293,000
PS17-03	Active Fault Location Study at Plant No. 2	Active	\$ 1,300,000
PS17-08	CEQA - Facilities Master Plan	Active	\$ 1,170,000
PS17-10	Emergency Overflow Weirs, Wing Wall Structural and Geotechnical Investigations	Active	\$ 465,000
PS18-01	Asset Management Plan Development	Active	\$ 420,000
PS18-05	Plant No. 2 Future Site Plan Development	Active	\$ 217,000
PS18-06	Go/No-Go Lights and Signage	Active	\$ 495,000
PS18-09	Ocean Outfall Condition Assessment and Scoping Study	Active	\$ 3,340,000
PS18-11	ETAP Model Updates for Plant Nos 1 and 2	Active	\$ 553,000
PS19-01	Digester 6 Pipe Stress Analysis at Plant No. 1	Active	\$ 45,000
PS19-02	Circular Primary Clarifier Replacement Phasing Study at Plant No 1	Active	\$ 53,000
Grand Total			\$ 22,129,700
Number of Chartered Projects			16
Board Approved Program Budget			\$ 28,652,000
Remaining Unallocated Budget			\$ 6,522,300

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020
Table 6 - Research Program Status Report**

Project Number	Project Name	Status	Allocated Budget
RE17-01	Operational Research Technical Support FY18-19	Active	\$ 650,000
RE17-02	Biogas Scrubber Evaluation	Active	\$ 865,000
RE17-03	Reliant Wet Well Wizard Test	Closed	\$ 45,013
RE17-04	AquaNereda Aerobic Granular Sludge Process	Active	\$ 242,000
RE17-05	Organica FCR Process	Active	\$ 242,000
RE17-06	TWAS Pump Reliability Improvement Trials at Plant No. 2	Closed	\$ 10,159
RE17-07	Super Oxygenation System Research at Seal Beach Pump Station	Closed	\$ 80,000
RE18-01	Trickling Filter Bleach Test at Plant No. 1	Active	\$ 140,000
RE18-02	Protein Matrix Demonstration Study at Plant No 1	Active	\$ 310,000
Grand Total			\$ 2,584,172
Number of Chartered Projects			9
Board Approved Program Budget			\$ 8,500,000
Remaining Unallocated Budget			\$ 5,915,828

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020
Table 7 - Small Construction Projects Program Status Report**

Project Number	Project Name	Status	Allocated Budget
FE10-21	Area 02 Craig Regional Park Manhole Improvements	Active	\$ 1,358,999
FE14-05	Plant No. 1 Fleet Services UST Leak Remediation	Active	\$ 1,487,311
FE15-07	Secondary Treatment and Plant Water VFD Replacement at Plant 1	Active	\$ 3,319,600
FE15-10	East Lido Force Main Rehabilitation	Active	\$ 2,228,000
FE16-06	Fuel Cell Facilities Demolition	Active	\$ 900,000
FE16-10	East Basin Distribution Box Repair	Active	\$ 1,021,960
FE16-11	Lane Channel Crossing	Active	\$ 500,000
FE16-14	Slater Pump Station Valve Replacements	Active	\$ 1,050,000
FE17-01	Carbon Canyon Pipeline Sag Repairs	Active	\$ 783,000
FE17-03	Battery Storage System at Plant No. 1	Active	\$ 571,000
FE17-05	Plant 1 ICS Network Extension	Active	\$ 950,000
FE18-06	CenGen Instrument Air Compressors Replacement at Plant No. 1 and No. 2	Active	\$ 1,450,000
FE18-08	West Trunk Bypass Sewer Realignment	Active	\$ 98,000
FE18-11	Headworks Explosive Gas Monitoring Systems at Plant No. 1 and No. 2	Active	\$ 335,000
FE18-12	Erosion Control at Santa Ana River and Hamilton Ave	Active	\$ 245,000
FE18-13	Redhill Relief Sewer Relocation at State Route 55	Active	\$ 1,540,000
FE18-14	Plant Water Pipeline Replacement in Kinnison, Lindstrom, and Scott Tunnels at Plant No. 2	Active	\$ 1,425,000
FE18-15	Plant Boiler System Relief at Plant No. 2	Active	\$ 180,000
FE18-16	Truck Loading Basement Drain Modifications at Plant No. 1	Active	\$ 440,000
FE18-17	Trunkline Sampler Power Feed at Plant No 2	Active	\$ 160,000
FE18-18	Portable Generator Connector at Lido Pump Station	Active	\$ 106,000
FE18-19	12KV Distribution B and East RAS Pump Station Roofing Replacement	Active	\$ 988,000
FE18-20	Blower Building No. 1 Air Compressors at Plant No. 1	Active	\$ 1,200,000
FE19-01	Pump Station Portable Generator Connectors	Active	\$ 1,990,000
FE19-02	Cengen Plant Water Pipe Replacement at Plant No. 1	Active	\$ 825,000
FE19-04	Sunflower Pump Replacement at Plant No. 1	Active	\$ 6,300,000
FE19-03	Trickling Filter Sludge and Scum Pumps Replacement at Plant No. 1	Active	\$ 700,000
FE19-05	Engineering Trailer B Car Chargers at Plant No. 1	Active	\$ 12,000
FE19-06	EPSA Motor Cooling Improvements at Plant No. 2	Active	\$ 403,000
Grand Total			\$ 32,566,870
Total Chartered Projects			29
Board Approved Program Budget			\$ 53,250,000
Remaining Unallocated Budget			\$ 20,683,130

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020
Table 8 - Information Technology Capital Program Status Report**

Project Number	Project Name	Status	Allocated Budget
IT16-03	Plant 2 Internet Connection	Active	\$ 50,000
IT16-05	Plant 2 Radio Repeater Upgrade	Closed	\$ 35,000
IT16-06	Network Equipment 2016-17	Closed	\$ 44,302
IT16-07	Server Replacement and Obsolescence	Closed	\$ 337,332
IT16-08	IT Security 2016-17	Active	\$ 162,000
IT16-09	iPACS Enhancements	Active	\$ 85,000
IT16-10	LIMS Compliance Improv Project	Active	\$ 754,800
IT16-11	Business Continuity Plan	Active	\$ 140,000
IT17-01	VMWare	Active	\$ 800,000
IT17-02	Upgrade Active Directory Directory to 2016	Active	\$ 56,000
IT17-03	Upgrade ShoreTel System Server	Active	\$ 190,000
IT17-04	PCI Improvements	Closed	\$ 131,093
IT17-05	Conference Room Monitor Upgrade	Active	\$ 75,686
IT17-06	Printer Obsolescence	Active	\$ 350,000
IT17-07	Safety Management Suite	Active	\$ 106,000
IT17-08	Perimeter Physical Security Im	Closed	\$ 170,077
IT17-09	MYOCSD Redesign	Closed	\$ 170,077
IT17-10	Electronic Operator Round Form	Active	\$ 45,000
IT17-11	P2 Radio Repeater	Closed	\$ 170,077
IT17-12	Sever/Network Power Improvements	Active	\$ 90,000
IT17-13	Graphric Workstations for PAO	Closed	\$ 15,000
IT17-14	Specialized Application Programing & Support	Active	\$ 600,000
IT17-15	Data Storage Replac/Obsolescens	Active	\$ 600,000
IT18-02	Fleet Management Information System	Active	\$ 250,000
IT18-03	Timecard Systems Upgrade	Active	\$ 150,000
IT18-04	Conference Rooms Audio System Replacement	Active	\$ 90,000
IT18-05	Trusted System Document Management	Active	\$ 100,000
IT18-06	Server Replacement and Obsolescence FY18/19-19/20	Active	\$ 900,000
IT18-07	Network Equipment FY18/19-19/20	Active	\$ 850,000
IT18-09	Records Management Information System	Active	\$ 100,000
IT18-10	Board Services Management System	Active	\$ 60,000
IT18-11	IT Security Budget 2018-2019	Active	\$ 150,000
Grand Total			\$ 7,827,444
Total Chartered Project			32
Board Approved Program Budget		\$	10,000,000
Remaining Unallocated Budget		\$	2,172,556

**Capital Improvement Program Contract Performance Report
for Quarter Ending 03/31/2020
Table 9 - Operations & Maintenance Capital Program Status Report**

Project Number	Project Name	Status	Allocated Budget
FR00001	SALS Hidrostal Pump	Active	\$ 212,268
FR00002	Chopper Pump at Dig P P2	Active	\$ 212,268
FR00008	Rag Bin Ramp Retrofit	Active	\$ 33,038
FR00011	Westside Impeller / Line Replacement	Active	\$ 108,368
SC16-01	Maint. Storage Area Tool Cage	Active	\$ 12,000
SC17-01	CENGEN #1 Elevator Rehab	Active	\$ 12,000
SC17-02	P1 CenGen Plant Water Piping Rehabilitation	Active	\$ 250,000
SC17-03	CenGen Oil Filter Platform	Active	\$ 260,000
SC17-04	P1 CenGen 12KV Circuit Breaker Replacement	Active	\$ 220,000
SC17-05	Hidrostal Pump - TEFC Close Coupled Motor #2 (Pump for SALS)	Active	\$ 261,260
SC17-06	P1 Lab UPS System Replacement	Active	\$ 290,294
SC18-01	P1 Primary Clarifier Fall Protection Improvements	Active	\$ 50,000
SC18-02	Joint Cen Gen Oil Centrifuge Heater & Controls Rehabilitation (MP-18)	Active	\$ 120,000
SC18-03	P1 SALS Main Duty Pump & Motor and Installation - Remaining 2 (MP-524)	Active	\$ 500,000
SC18-04	Edinger UPS Replacement (MP-444)	Active	\$ 15,000
SC18-05	P1 Laboratory HVAC Boiler Burner Replacement At Plant No.1	Active	\$ 400,461
SC18-06	Pump Station Bypass Parts - Procurement (MP-426)	Active	\$ 500,000
SC18-08	MacArthur Pump Station - FM Valve Replacement	Active	\$ 55,109
SC18-09	Admin Bldg UPS System Replacement	Active	\$ 185,000
SC18-10	P2 South Scrubber Complex Bleach Pump Turndown (MP-420)	Active	\$ 44,900
Grand Total			\$ 3,697,066
Total Chartered Projects			20
Board Approved Program Budget		\$	15,622,000
Remaining Unallocated Budget		\$	11,880,034



ORANGE COUNTY SANITATION DISTRICT
Capital Improvement Program
Contract Performance Report
 For the period ending March 31, 2020

PART 4 – SUPPLEMENTAL ENGINEERING SERVICES CONTRACT

In May 2016, the Sanitation District Board of Directors approved a \$41 million professional services agreement with Jacobs Project Management Co. to provide supplemental engineering and support staff services for a four-year term with the option of three one-year renewals. The benefits of using a supplemental engineering services contract, as opposed to hiring full-time staff or limited-term employees, include rapid mobilization of highly skilled/technical staff, flexibility to change the mix of staff positions on an immediate and as-needed basis, the ability to reduce staff as workloads decrease, access to technical experts to support special tasks, and access to staff with wastewater project experience.

A status table for the supplemental engineering services contract summary is attached under Table 10, and the supplemental engineering services labor summary can be found under Table 11.

Table 10 – Supplemental Engineering Services Contract Status

	Total Fees	Time
Contract	\$41,000,000	86 months ⁽¹⁾
Actuals to Date	\$19,987,641 49%	47 months 48%
Remaining	\$21,012,359 51%	39 months 52%

⁽¹⁾ Assuming three 1-year extensions

Table 11 - Supplemental Engineering Services Labor Summary

	This Quarter	Inception to Date
Labor Hours	8,519	149,061
Full Time Equivalent	18.9	21.1
Labor Costs (no expenses)	\$1,133,618	\$19,568,496
Average Hourly Rate	\$133	\$131
