



**ORANGE COUNTY SANITATION DISTRICT**  
**Capital Improvement Program**  
**Contract Performance Report**  
For the period ending June 30, 2020

DATE: August 18, 2020

TO: Orange County Sanitation District  
Board of Directors

FROM: James D. Herberg, General Manager  
Through: Kathy Millea, Director of Engineering

This report summarizes the status, activities, and performance of public works construction contracts and consultant agreements. This report also identifies the names and status of projects being performed under master budgets for planning studies, research, small construction projects, O&M capital projects, and information technology projects.

**Table of Contents**

<u>Part 1 – Construction Contracts</u>	page 2
Active Construction Contracts	
Construction Contracts Closed in Last Quarter	
Cumulative Change Order Rates – Closed Construction Contracts	
<u>Part 2 – Engineering Services Agreements</u>	page 7
Active Engineering Services Agreements	
Active Task Orders by Master Agreement	
<u>Part 3 - Master Budget Projects</u>	page 11
Planning Studies Status Report	
Research Program Status Report	
Small Construction Projects Program Status Report	
Information Technology Capital Program Status Report	
Operations and Maintenance Capital Program Status Report	
<u>Part 4 - Supplemental Engineering Services Contract</u>	page 17
Supplemental Engineering Services Contract Status	
Supplemental Engineering Services Contract Labor Summary	




# ORANGE COUNTY SANITATION DISTRICT Capital Improvement Program Contract Performance Report

For the period ending June 30, 2020

## PART 1 - CONSTRUCTION CONTRACTS

Table 1 lists the construction contracts active as of June 30, 2020. The graph below shows the number and total value of projects broken down plant and collections.

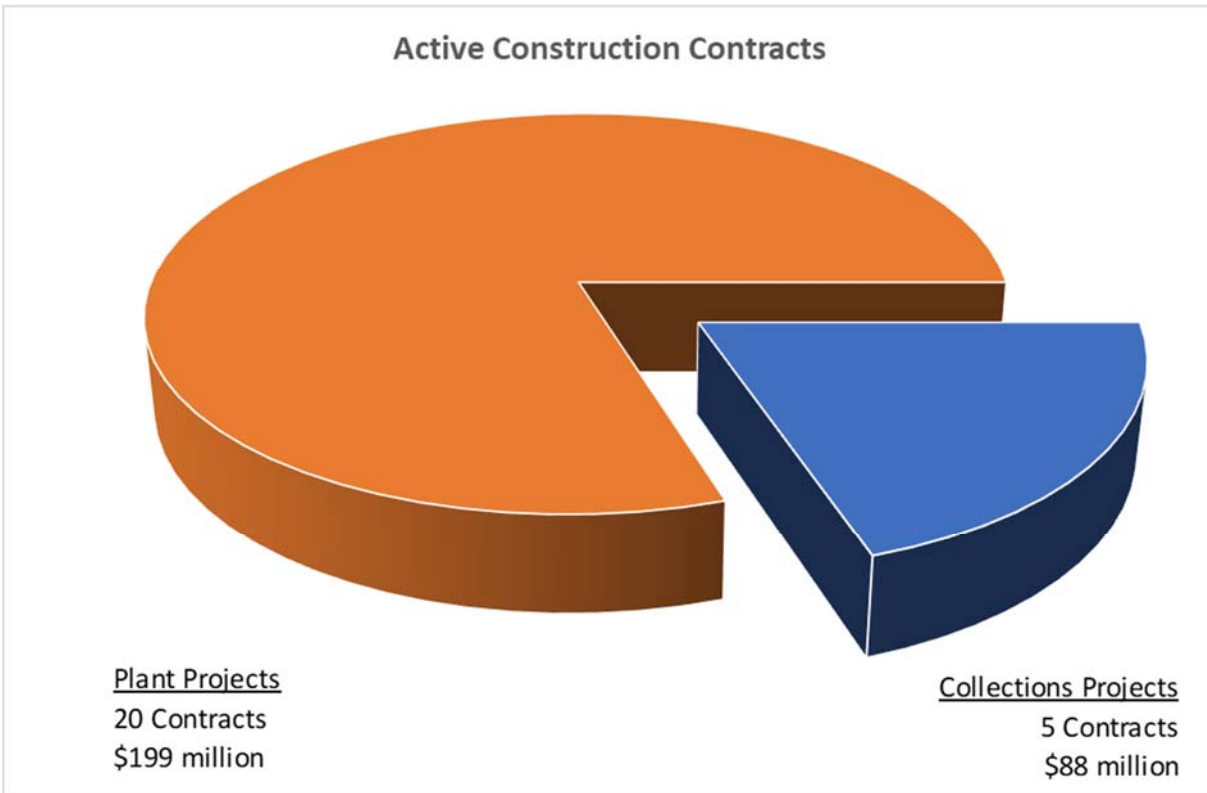

Three construction contracts were closed in this quarter, as listed in Table 2.

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 1 - Active Construction Contracts**

Project / Contract	Contractor	Award Date	Board Award Amount	Change Orders	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
<b>2-72</b> Newhope-Placentia Trunk Replacement 2-72B Newhope-Placentia Trunk Replacement, Segment B	OHL USA, INC.	06/15/2018	\$58,242,000	\$1,524,368	\$59,766,368	6.5%	6.5%	2.6%	3.9%
<b>3-62</b> Westminster Blvd Force Main Replacement 3-62 Westminster Blvd Force Main Replacement	Teichert Energy & Utilities Group, Inc.	12/18/2019	\$27,743,000	\$0	\$27,743,000	10.0%	10.0%	0.0%	10.0%
<b>J-117</b> Ocean Outfall System Rehabilitation J-117B Outfall Low Flow Pump Station	Shimmick Construction Co., Inc.	12/19/2018	\$90,200,000	\$176,877	\$90,376,877	8.0%	8.0%	0.2%	7.8%
<b>J-126</b> Safety Improvements Program J-126C NFPA 820 HVAC and Electrical Improvements J-126K Stairs, Hatches, Walkway Hazards, Ladders, Guardrails, Roof Fall Protection	MMC, Inc. Olsson Construction, Inc.	03/05/2019 10/24/2018	\$469,000 \$3,637,601	\$0 \$917	\$469,000 \$3,638,518	10.0% 10.0%	10.0% 10.0%	0.0% 0.0%	10.0% 10.0%
<b>M-FE</b> Small Construction Projects Program FE17-01 Carbon Canyon Pipeline Sag Repairs FE18-11 Headworks Explosive Gas Monitoring Systems at Plant No. 1 and No. 2	Tharsos, Inc. Mike Pritch and Sons, Inc. Baker Electric	10/24/2018 10/02/2019 01/22/2020	\$785,000 \$510,000 \$223,984	\$19,905 \$0 \$0	\$786,000 \$510,000 \$223,984	10.0% 10.0% 10.0%	10.0% 10.0% 10.0%	2.5% 0.0% 0.0%	7.5% 10.0% 10.0%
<b>M-FR-820</b> Master Operationally Funded FE17-06 Tustin Ave Manhole and Pipe Repair M-FR-880 Master Operationally Funded MP-105 P2 CENGEN Steam Turbine Rehabilitation MP-248 P2 Secondary Clarifier Repairs (AS Plant) MP-509 P2 Headworks Low Voltage Cable Assessment MP-638 Activated Sludge Plant Clarifier Inlet Gate Replacement at Plant No. 2	M. Brey Electric, Inc. M. Brey Electric, Inc. O'Connell Engineering & Construction, Inc. Nuline Technologies, LLC Dresser-Rand W. M. Lyles Company Mass Electric Construction Co. Innovative Construction Solutions	03/25/2020 09/17/2019 05/27/2020 10/24/2019 03/25/2018 06/26/2019 12/18/2019 12/18/2019	\$101,050 \$42,285 \$674,800 \$350,000 **\$484,220 \$3,048,000 \$434,327 \$658,300	\$0 \$0 \$0 \$0 \$0 \$42,255 \$0 \$0	\$101,050 \$42,285 \$674,800 \$350,000 \$484,220 \$3,090,255 \$434,327 \$658,300	20.0% 20.0% 10.0% 10.0% 20.0% 20.0% 20.0% 20.0%	20.0% 20.0% 10.0% 10.0% 2.5% 10.0% 20.0% 10.0%	0.0% 0.0% 0.0% 0.0% 0.0% 1.4% 0.0% 0.0%	20.0% 20.0% 10.0% 10.0% 2.5% 10.0% 20.0% 10.0%
<b>M-SM-CAP</b> Operations & Maintenance Capital Program SC17-03 CenGen Oil Filter Platform	Metro Builders & Engineers Group, Ltd.	12/04/2019	\$134,479	\$10,968	\$134,479	10.0%	10.0%	8.2%	1.8%
<b>P1-115</b> Title 24 Access Compliance and Building Rehabilitation Project P1-115B Rehabilitation of Fleet Services Building, Building 8 and Paving Area	ODC Engineering & Technology	09/11/2017	\$2,235,563	\$61,194	\$2,296,757	10.0%	10.0%	2.7%	7.3%
<b>P1-128</b> Headquarters Complex P1-128C Headquarters Complex Site Preparation	Resource Environmental, Inc.	6/24/2020	\$1,555,000	\$0	\$1,555,000	10.0%	10.0%	0.0%	10.0%
<b>P1-129</b> Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1 P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1	Abhe & Svoboda, Inc.	07/24/2019	\$6,863,092	\$0	\$6,863,092	10.0%	10.0%	0.0%	10.0%
<b>P2-122</b> Headworks Modifications at Plant No. 2 for GWRS Final Expansion P2-122 Headworks Modifications at Plant No. 2 for GWRS Final Expansion	Shimmick Construction Co., Inc.	01/22/2020	\$14,487,735	\$0	\$14,487,735	10.0%	10.0%	0.0%	10.0%

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 1 - Active Construction Contracts**

Project / Contract	Contractor	Award Date	Board Award Amount	Change Orders	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
<b>P2-123</b> Return Activated Sludge Piping Replacement at Plant 2 P2-123 Return Activated Sludge Piping Replacement at Plant 2	Shimmick Construction Co., Inc.	09/25/2019	\$6,042,110	\$0	\$6,042,110	10.0%	10.0%	0.0%	10.0%
<b>P2-92</b> Sludge Dewatering and Odor Control at Plant 2 P2-92 Sludge Dewatering and Odor Control at Plant 2	Shimmick Construction Co., Inc.	01/12/2015	\$49,850,000	-\$2,530,887	\$52,380,887	5.0%	6.0%	5.1%	0.9%
<b>P2-98</b> Primary Treatment Rehabilitation at Plant No. 2 P2-98B B/C-Side Primary Clarifiers Interim Repair at Plant 2	Myers & Sons Construction, LLC	01/23/2019	\$8,665,000	\$38,833	\$8,703,833	10.0%	10.0%	0.4%	9.6%
<b>M-FR-870</b> Master Operationally Funded MP-276 Central Generation Engine Overhauls at Plant No. 1 and Plant No. 2	UPS Midstream Services, Inc.	10/23/2019	\$5,636,335	\$0	\$5,636,335	20.0%	20.0%	0.0%	20.0%
<b>Total</b>			<b>\$283,073,881</b>	<b>\$4,406,204</b>	<b>\$287,449,212</b>				

\*\* Original Award was \$245,424, and later amended to \$484,220 with a contingency reduction by Board Action on 4/22/20






# ORANGE COUNTY SANITATION DISTRICT Capital Improvement Program Contract Performance Report

For the period ending June 30, 2020

When the Sanitation District Board awards a construction contract, they also approve a contingency which allows the General Manager to approve contract change orders up to the amount of the contingency. One purpose of this report is to document how much of the contingency is utilized. A contract's change order rate is only meaningful when the work is completed. As such, the change order performance charts in this report are based only on contracts closed since the Board began approving contingencies in 2008. The following chart shows how cumulative change order rates have changed for plant, collections, and all contracts since the contingency system was implemented.

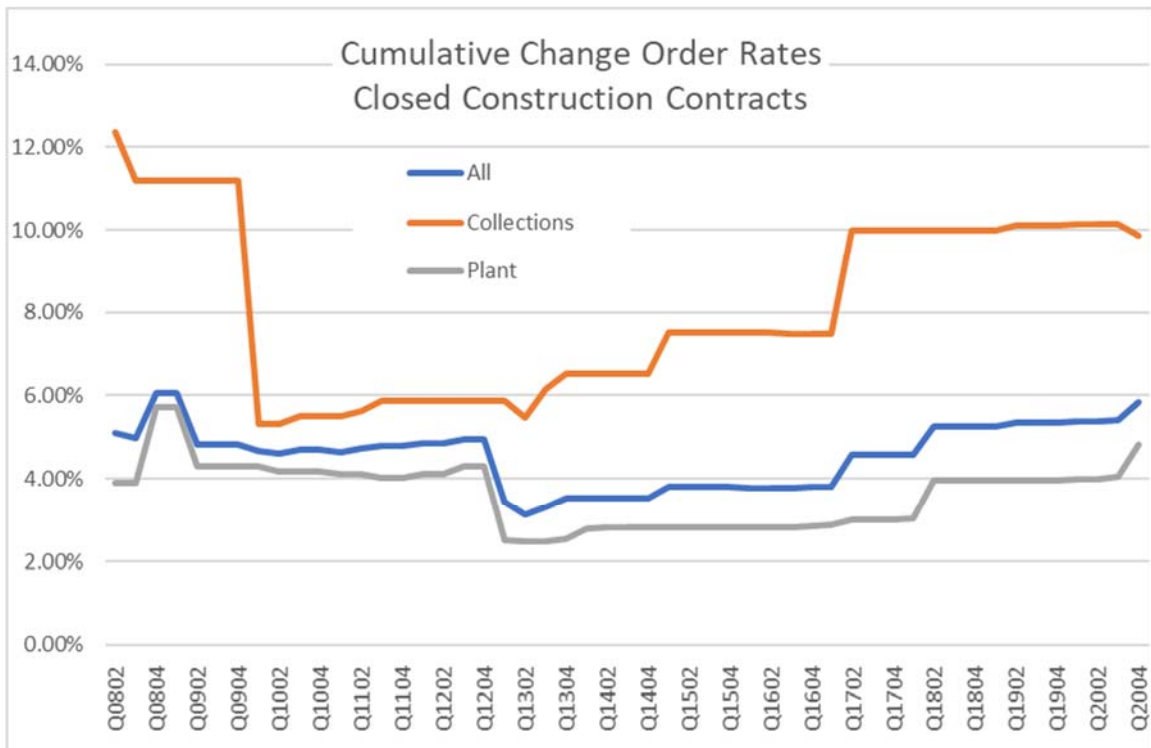



# **ORANGE COUNTY SANITATION DISTRICT**

## **Capital Improvement Program**

### **Contract Performance Report**

For the period ending June 30, 2020

## **PART 2 – ENGINEERING SERVICES AGREEMENTS**

The Sanitation District engages engineering consultants through Professional Service Agreements (PSAs), Professional Design Services Agreements (PDSAs), Professional Construction Services Agreements (PCSAs), and Master Professional Services Agreements (Master Agreements). PDSAs are used to obtain design engineering services, and PCSAs are a subsequent agreement with the design consultant to provide support services during construction. PSAs are used for planning studies and other consultant assignments.

Master Agreements are issued to a pool of pre-qualified consultants for smaller projects. On those smaller projects, the Sanitation District solicits task order proposals from three or four of the firms and awards a task order to the most qualified consultant. There are currently six sets of Master Agreements.

- 2012 Master Design Agreements (expired)
- 2015 Master Design Agreements (expired)
- 2018 Master Design Agreements
- 2017 Master Agreements for CEQA Studies
- 2017 Master Agreements for Collection Planning Studies
- 2017 Master Agreements for Wastewater Treatment Planning Studies

The two Master Design Agreements from 2012, and 2015 have expired, meaning no new task orders can be issued under them, but previously-issued task orders remain active until completed. Task Orders are limited by Sanitation District Ordinance No. OCSD-52 \$300,000 per task order.

A status table for all Active Engineering Services Agreements (PDSAs and PCSAs) is attached under Table 3, and a status table for all Active Task Orders by Master Agreement is attached under Table 4 (Master Agreements).

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 3 - Active Engineering Services Agreements**

Project / Contract	Type	Consultant	Award Date	Board Award Amount	Amendments	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
<b>2-41-8 SARI Rock Stabilizers Removal</b>	PCSA	Michael Baker International, Inc.	09/26/2018	\$215,129	\$0	\$215,129	10.0%	10.0%	0.0%	10.0%
<b>2-72 Newhope-Placentia Trunk Replacement</b>	PCSA	Lee & Ro	03/23/2016	\$3,253,946	\$0	\$3,253,946	10.0%	10.0%	0.0%	10.0%
<b>3-62 Westminster Blvd Force Main Replacement</b>	PCSA	Stantec Consulting Services, Inc.	12/18/2019	\$1,183,000	\$0	\$1,183,000	10.0%	10.0%	0.0%	10.0%
<b>3-62 Westminster Blvd Force Main Replacement</b>	PDSA	Stantec Consulting Services, Inc.	07/22/2015	\$6,917,175	-\$1,339,457	\$5,577,718	10.0%	10.0%	0.0%	10.0%
<b>3-64 Rehabilitation of Western Regional Sewers</b>	PDSA	AECOM Technical Services, Inc.	01/27/2016	\$17,639,250	\$1,088,654	\$18,727,904	10.0%	10.0%	6.2%	3.8%
<b>3-67 Seal Beach Pump Station Replacement</b>	PDSA	Lee & Ro	11/20/2019	\$5,947,850	\$0	\$5,947,850	10.0%	10.0%	0.0%	10.0%
<b>5-60 Newport Force Main Rehabilitation</b>	PCSA	Brown and Caldwell	04/29/2014	\$2,231,925	\$839,714	\$3,071,639	8.0%	38.7%	37.6%	1.0%
<b>5-67 Bay Bridge Pump Station Replacement</b>	PDSA	Arcadis US Inc.	10/25/2017	\$7,137,000	\$493,983	\$7,505,955	10.0%	10.0%	6.9%	3.1%
<b>6-17 District 6 Trunk Sewer Relief</b>	PCSA	RMC Water & Environment	10/10/2016	\$290,000	\$0	\$290,000	15.0%	15.0%	0.0%	15.0%
<b>7-66 Sunflower and Red Hill Interceptor Repairs</b>	PDSA	GHD	09/25/2019	\$308,712	\$0	\$308,712	10.0%	10.0%	0.0%	10.0%
<b>J-117 Ocean Outfall System Rehabilitation</b>	PCSA	Brown and Caldwell	05/24/2018	\$1,121,666	\$112,167	\$1,233,833	10.0%	10.0%	10.0%	0.0%
<b>J-117A Interplant Effluent Pipeline Rehabilitation</b>	PCSA	Brown and Caldwell	12/19/2018	\$8,363,913	\$346,857	\$8,910,770	10.0%	10.0%	4.1%	5.9%
<b>J-124 Digester Gas Facilities Rehabilitation</b>	PDSA	Brown and Caldwell	11/15/2017	\$1,770,000	-\$36,411	\$1,173,389	10.0%	10.0%	0.0%	10.0%
<b>J-126 Safety Improvements Program</b>	PDSA	Arcadis	08/29/2016	**\$3,040,000	\$0	\$3,040,000	10.0%	10.0%	0.0%	10.0%
<b>J-98 Electrical Power Distribution System Improvements</b>	PDSA	Brown and Caldwell	01/29/2020	\$2,240,000	\$0	\$2,240,000	10.0%	10.0%	0.0%	10.0%
<b>M-FE Small Commercial Projects Program</b>	PSA	HDR Engineering, Inc.	06/28/2017	\$131,939	\$0	\$131,939	10.0%	10.0%	0.0%	10.0%
<b>M-RESEARCH Program</b>	PSA	Carollo Engineers, Inc.	04/21/2017	\$656,783	\$63,097	\$719,880	15.0%	15.0%	9.6%	5.4%
<b>M-STUDIES/Planning Studies Program</b>	PSA	Lockwood, Andrews & Newman, Inc.	12/20/2017	\$505,042	\$0	\$505,042	10.0%	10.0%	0.0%	10.0%
<b>PS15-02 Edinger Pump Station Rehabilitation Study</b>	PSA	Geosyntec Consultants, Inc.	06/28/2017	\$2,578,028	\$132,425	\$2,710,453	10.0%	10.0%	5.1%	4.9%
<b>PS15-06 Seismic Evaluation of Structures at Plant Nos. 1 and 2</b>	PSA	RMC Water & Environment	08/24/2016	\$2,802,675	\$19,372	\$2,822,047	10.0%	10.0%	0.7%	9.3%
<b>PS16-01 Stormwater Master Plan</b>	PSA	Michael Baker International, Inc.	07/26/2017	\$715,300	\$54,839	\$770,139	10.0%	10.0%	7.7%	2.3%
<b>PS17-03 Active Fault Location Study at Plant No. 2</b>	PSA	Lettis Consultants International, Inc.	03/06/2019	\$868,286	\$0	\$868,286	10.0%	10.0%	0.0%	10.0%
<b>PS17-08 CEQA - Facilities Master Plan</b>	PSA	Dudek	02/27/2019	\$812,709	\$0	\$812,709	10.0%	10.0%	0.0%	10.0%
<b>PS18-09 Ocean Outfall Condition Assessment and Scoping Study</b>	PSA	Carollo Engineers, Inc.	03/25/2020	\$2,744,000	\$0	\$2,744,000	10.0%	10.0%	0.0%	10.0%
<b>P1-101 Sludge Dewatering and Odor Control at Plant 1</b>	PCSA	HDR Engineering, Inc.	06/28/2012	\$7,140,000	\$2,453,653	\$9,593,653	8.0%	35.0%	34.4%	0.6%
<b>P1-105 Headworks Rehabilitation at Plant 1</b>	PDSA	Carollo Engineers, Inc.	05/27/2015	\$17,528,957	\$7,744,413	\$25,273,370	10.0%	51.0%	44.2%	6.8%
<b>P1-128 Headworks Complex</b>	PDSA	HDR Engineering, Inc.	06/22/2016	\$11,785,709	-\$752,553	\$11,033,156	10.0%	10.0%	0.0%	10.0%
<b>P1-128 Headworks Complex</b>	PSA	LSA Associates, Inc.	08/11/2016	\$420,927	\$0	\$420,927	10.0%	10.0%	0.0%	10.0%
<b>P1-128C Headworks Complex Site Preparation</b>	PCSA	HDR Engineering, Inc.	6/24/2020	\$1,78,000	\$0	\$1,78,000	10.0%	10.0%	0.0%	10.0%
<b>P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1</b>	PCSA	AECOM Technical Services, Inc.	07/24/2019	\$140,000	\$0	\$140,000	10.0%	10.0%	0.0%	10.0%
<b>P1-129 Return Activated Sludge Piping Replacement at Activated Sludge Plant No. 1</b>	PDSA	AECOM Technical Services, Inc.	06/20/2017	\$523,039	\$27,015	\$550,054	10.0%	10.0%	5.2%	4.8%



**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 3 - Active Engineering Services Agreements**

Project / Contract	Type	Consultant	Award Date	Board Award Amount	Amendments	Current Contract Amount	Original Contingency	Current Contingency	Contingency Used	Contingency Remaining
<b>P1-132</b> Uninterruptable Power Supply Improvements at Plant 1 P1-132 Uninterruptable Power Supply Improvements at Plant 1	PDSA	Tetra Tech, Inc.	10/23/2019	\$784,680	\$0	\$784,680	10.0%	10.0%	0.0%	10.0%
<b>P1-133</b> Primary Sedimentation Basins No. 6-31 Reliability Improvements at Plant No. 1 P1-133 Primary Sedimentation Basins No. 6-31 Reliability Improvements at Plant No. 1	PDSA	Carollo Engineers, Inc.	09/25/2019	\$1,219,667	\$0	\$1,219,667	10.0%	10.0%	0.0%	10.0%
<b>P2-110</b> Consolidated Demolition and Utility Improvements at Plant 2 P2-110 Consolidated Demolition and Utility Improvements at Plant 2	PCSA	Stantec Consulting Services, Inc.	01/25/2017	\$1,499,839	\$0	\$1,499,839	10.0%	10.0%	0.0%	10.0%
<b>P2-122</b> Headworks Modifications at Plant No. 2 for GWRS Final Expansion P2-122 Headworks Modifications at Plant No. 2 for GWRS Final Expansion	PCSA	CDM Smith Inc.	01/15/2020	\$2,200,000	\$0	\$2,200,000	10.0%	10.0%	0.0%	10.0%
<b>P2-123</b> Return Activated Sludge Piping Replacement at Plant 2 P2-123 Return Activated Sludge Piping Replacement at Plant 2	PCSA	SPEC Services, Inc.	09/25/2019	\$252,329	\$0	\$252,329	10.0%	10.0%	0.0%	10.0%
<b>P2-123</b> Return Activated Sludge Piping Replacement at Plant 2 P2-123 Return Activated Sludge Piping Replacement at Plant 2	PDSA	SPEC Services, Inc.	02/15/2018	\$668,217	\$0	\$668,217	10.0%	10.0%	0.0%	10.0%
<b>P2-124</b> Interim Food Waste Receiving Facility P2-124 Interim Food Waste Receiving Facility	PDSA	Kennedy/Jenks Consultants	09/05/2018	\$695,000	\$20,717	\$715,717	10.0%	10.0%	3.0%	7.0%
<b>P2-92</b> Sludge Dewatering and Odor Control at Plant 2 P2-92 Sludge Dewatering and Odor Control at Plant 2	PCSA	Brown and Caldwell	12/17/2014	\$4,798,328	\$0	\$4,798,328	10.0%	10.0%	0.0%	10.0%
<b>P2-98</b> Primary Treatment Rehabilitation at Plant No. 2 P2-98 Primary Treatment Rehabilitation at Plant No. 2	PDSA	Black & Veatch	07/27/2016	\$18,141,423	\$1,279,488	\$19,420,911	10.0%	10.0%	7.1%	2.9%
<b>P2-98B</b> B/C-Side Primary Clarifiers Interim Repair at Plant 2 P2-98B B/C-Side Primary Clarifiers Interim Repair at Plant 2	PCSA	Black & Veatch	01/23/2019	\$549,534	\$0	\$549,534	10.0%	10.0%	0.0%	10.0%
<b>SP-152</b> Climate Resiliency Study SP-152 Climate Resiliency Study	PSA	Hazen and Sawyer	11/28/2018	\$697,952	\$64,199	\$762,151	10.0%	10.0%	9.2%	0.8%
<b>SP-196</b> Process Control Systems Upgrades Study SP-196 Process Control Systems Upgrades Study	PSA	Stantec Consulting Services, Inc.	03/01/2018	\$1,389,866	\$9,000	\$1,398,866	10.0%	10.0%	0.6%	9.4%
<b>Total</b>				<b>\$154,287,795</b>	<b>\$12,621,172</b>	<b>\$166,788,939</b>				

\*\* Original Award was \$1,540,000, and later amended to \$3,040,000 by Board Action

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 4 - Active Task Orders by Master Agreement**

Master Agreement / Project	Consultant	Award Date	Original Task Order Value	Amendments	Current Task Order Value
<b>2012 Master Professional Design Service Agreements (Expired)</b>					
FE10-21 Area 02 Craig Regional Park Manhole Improvements	GHD	10/8/2012	\$58,440	\$41,560	\$100,000
<b>2015 Master Professional Design Service Agreements (Expired)</b>					
FE14-05 Plant No. 1 Fleet Services UST Leak Remediation	Dudek	9/1/2015	\$86,116	\$73,137	\$159,253
<b>2017 Master Agreements for Waste Water Treatment Planning Studies</b>					
PS17-10 Emergency Overflow Weirs, Wing Wall Structural and Geotechnical Investigations	HDR Engineering, Inc.	05/21/2019	\$260,415	\$0	\$260,415
PS18-05 Plant No. 2 Future Site Plan Development	Brown and Caldwell	05/22/2019	\$122,389	\$0	\$122,389
PS18-11 ETAP Model Updates for Plant Nos 1 and 2	Brown and Caldwell	3/17/2020	\$227,412	\$0	\$227,412
<b>2017 Master Agreements for Collection Planning Studies</b>					
No Task Orders issued to Date	--	--	--	--	--
<b>2017 Master Agreements for CEQA Studies</b>					
No Task Orders issued to Date	--	--	--	--	--
<b>2018 Master Professional Design Service Agreements</b>					
FE18-06 CenGen Instrument Air Compressors Replacement at Plant No. 1 and No. 2	IDS Group, Inc.	04/28/2020	\$89,876	\$0	\$89,876
FE18-13 Redhill Relief Sewer Relocation at State Route 55	GHD, Inc.	3/27/2020	\$168,612	\$0	\$168,612
FE18-14 Plant Water Pipeline Replacement in Kinnison, Lindstrom, and Scott Tunnels at Plant No. 2	Dudek	11/6/2019	\$108,308	\$0	\$108,308
FE18-15 Plant Boiler System Relief at Plant No. 2	IDS Group, Inc.	10/22/2019	\$23,299	\$0	\$23,299
FE18-16 Truck Loading Basement Drain Modifications at Plant No. 1	GHD, Inc.	12/4/2019	\$70,130	\$0	\$70,130
FE18-19 12KV Distribution Center B and East RAS Pump Station Roof Replacement	HDR Engineering, Inc.	09/16/2019	\$74,771	\$8,672	\$83,443
FE19-02 Cengen Plant Water Pipe Replacement at Plant No. 1	AECOM	04/30/2020	\$156,498	\$0	\$156,498
FE19-06 EPSA Motor Cooling Improvements at Plant No. 2	IDS Group, Inc.	05/05/2020	\$88,206	\$0	\$88,206
FR2-0013 Trickling Filter Sludge Pump Room Exhaust Fan Relocation at Plant No. 2	AECOM	11/6/2019	\$75,120	\$0	\$75,120
J-127 Natural Gas Pipelines Replacement at Plant Nos. 1 and 2	Black & Veatch	1/21/2019	\$271,964	\$0	\$271,964
P1-135 Digester Ferric Chloride Piping Replacement at Plant No. 1	Dudek	2/19/2020	\$127,174	\$0	\$127,174
<b>Total</b>			\$2,008,730	\$123,369	\$2,132,099



# **ORANGE COUNTY SANITATION DISTRICT**

## **Capital Improvement Program**

### **Contract Performance Report**

For the period ending June 30, 2020

### **PART 3 – MASTER BUDGET PROJECTS**

The Board-adopted budget for Fiscal Years 2018-19 and 2019-20 includes master program budgets that allow staff to more quickly initiate, execute, and manage smaller projects that fit within the scope of a particular program. The projects chartered under these program budgets are referred to as sub-projects and are managed to the same standards as projects specifically listed in the adopted budget. A status table for each of these programs listing the sub-projects is attached.

<b>Master Program Title</b>	<b>Status Table</b>
Planning Studies Program	Table 5
Research Program	Table 6
Small Construction Projects Program	Table 7
Information Technology Capital Program	Table 8
Operations & Maintenance Capital Program	Table 9

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020  
Table 5 - Planning Studies Status Report**

Project Number	Project Name	Status	Allocated Budget
PS15-02	Edinger Pump Station Rehabilitation Study	Active	\$ 971,000
PS15-06	Seismic Evaluation of Structures at Plant Nos. 1 and 2	Active	\$ 3,860,000
PS15-08	Collections Capacity Evaluation Study	Active	\$ 3,682,000
PS15-10	2017 Facilities Master Plan	Closed	\$ 3,820,824
PS16-01	Stormwater Master Plan	Active	\$ 1,415,700
PS16-02	SCE Feed Reliability Improvements Study	Active	\$ 293,000
PS17-03	Active Fault Location Study at Plant No. 2	Active	\$ 1,300,000
PS17-08	CEQA - Facilities Master Plan	Active	\$ 1,247,000
PS17-10	Emergency Overflow Weirs, Wing Wall Structural and Geotechnical Investigations	Active	\$ 465,000
PS18-01	Asset Management Plan Development	Closed	\$ 331,035
PS18-05	Plant No. 2 Future Site Plan Development	Active	\$ 217,000
PS18-06	Go/No-Go Lights and Signage	Active	\$ 495,000
PS18-09	Ocean Outfall Condition Assessment and Scoping Study	Active	\$ 3,340,000
PS18-11	ETAP Model Updates for Plant Nos 1 and 2	Active	\$ 553,000
PS19-01	Digester 6 Pipe Stress Analysis at Plant No. 1	Active	\$ 45,000
PS19-02	Circular Primary Clarifier Replacement Phasing Study at Plant No 1	Closed	\$ 43,269
PS19-03	Laboratory Rehabilitation Feasibility Study	Active	\$ 450,000
PS19-04	Chemical Evaluation Study at Plant No 1 and 2	Closed	\$ 977
PS19-05	Collection System Flow Level Monitoring Study	Closed	\$ -
<b>Grand Total</b>			<b>\$ 22,529,805</b>
Number of Chartered Projects			19
Board Approved Program Budget		\$	28,652,000
Remaining Unallocated Budget		\$	6,122,195

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020**

**Table 6 - Research Program Status Report**

<b>Project Number</b>	<b>Project Name</b>	<b>Status</b>	<b>Allocated Budget</b>
RE17-01	Operational Research Technical Support FY18-19	Closed	\$ 656,506
RE17-02	Biogas Scrubber Evaluation	Active	\$ 865,000
RE17-03	Reliant Wet Well Wizard Test	Closed	\$ 45,013
RE17-04	AquaNereda Aerobic Granular Sludge Process	Closed	\$ 19,628
RE17-05	Organica FCR Process	Closed	\$ 15,564
RE17-06	TWAS Pump Reliability Improvement Trials at Plant No. 2	Closed	\$ 10,159
RE17-07	Super Oxygenation System Research at Seal Beach Pump Station	Closed	\$ 80,000
RE18-01	Trickling Filter Bleach Test at Plant No. 1	Closed	\$ 109,068
RE18-02	Protein Matrix Demonstration Study at Plant No 1	Active	\$ 310,000
RE19-01	Primary Scum Equipment Evaluation at Plant No. 1	Active	\$ 31,000
<b>Grand Total</b>			<b>\$ 2,141,938</b>
Number of Chartered Projects			10
Board Approved Program Budget			\$ 8,500,000
Remaining Unallocated Budget			\$ 6,358,062

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020  
Table 7 - Small Construction Projects Program Status Report**

Project Number	Project Name	Status	Allocated Budget
FE10-21	Area 02 Craig Regional Park Manhole Improvements	Active	\$ 1,359,000
FE14-05	Plant No. 1 Fleet Services UST Leak Remediation	Active	\$ 1,487,311
FE15-07	Secondary Treatment and Plant Water VFD Replacement at Plant 1	Active	\$ 3,319,600
FE15-10	East Lido Force Main Rehabilitation	Active	\$ 2,228,000
FE16-06	Fuel Cell Facilities Demolition	Closed	\$ 960,000
FE16-10	East Basin Distribution Box Repair	Closed	\$ 1,013,850
FE16-11	Lane Channel Crossing	Active	\$ 500,000
FE16-14	Slater Pump Station Valve Replacements	Closed	\$ 946,940
FE17-01	Carbon Canyon Pipeline Sag Repairs	Active	\$ 873,000
FE17-03	Battery Storage System at Plant No. 1	Active	\$ 612,000
FE17-05	Plant 1 ICS Network Extension	Active	\$ 950,000
FE18-06	CenGen Instrument Air Compressors Replacement at Plant No. 1 and No. 2	Active	\$ 1,450,000
FE18-08	West Trunk Bypass Sewer Realignment	Active	\$ 158,000
FE18-11	Headworks Explosive Gas Monitoring Systems at Plant No. 1 and No. 2	Active	\$ 470,000
FE18-12	Erosion Control at Santa Ana River and Hamilton Ave	Active	\$ 245,000
FE18-13	Redhill Relief Sewer Relocation at State Route 55	Active	\$ 1,540,000
FE18-14	Plant Water Pipeline Replacement in Kinnison, Lindstrom, and Scott Tunnels at Plant No. 2	Active	\$ 1,425,000
FE18-15	Plant Boiler System Relief at Plant No. 2	Active	\$ 180,000
FE18-16	Truck Loading Basement Drain Modifications at Plant No. 1	Active	\$ 440,000
FE18-17	Trunkline Sampler Power Feed at Plant No 2	Active	\$ 215,000
FE18-18	Portable Generator Connector at Lido Pump Station	Active	\$ 106,000
FE18-19	12KV Distribution B and East RAS Pump Station Roofing Replacement	Active	\$ 988,000
FE18-20	Blower Building No. 1 Air Compressors at Plant No. 1	Active	\$ 1,200,000
FE19-01	Pump Station Portable Generator Connectors	Active	\$ 1,990,000
FE19-02	Cengen Plant Water Pipe Replacement at Plant No. 1	Active	\$ 2,250,000
FE19-03	Trickling Filter Sludge and Scum Pumps Replacement at Plant No. 1	Active	\$ 1,100,000
FE19-04	Sunflower Pump Replacement at Plant No. 1	Active	\$ 6,300,000
FE19-05	Engineering Trailer B Car Chargers at Plant No. 1	Active	\$ 12,000
FE19-06	EPSA Motor Cooling Improvements at Plant No. 2	Active	\$ 550,000
FE19-08	Secondary Treatment VFD Replacements at Plant No. 2	Active	\$ 3,337,000
FE19-09	Newhope - Placentia Trunk Grade Separation Replacement Repairs	Active	\$ 500,000
FE19-10	Digesters C, D, F, G and I Gas Balance Lines Replacement at Plant No. 2	Active	\$ 200,000
FE19-11	Primary Clarifiers Nos. 6-31 Lighting and Alarm Improvements at Plant No. 1	Active	\$ 1,250,000
FE19-12	Rebuild Shop Fume Extractor Installation at Plant No 1	Active	\$ 325,000
FE19-13	VFD Replacements at Seal Beach Pump Station	Active	\$ 690,000
<b>Grand Total</b>			<b>\$ 41,170,701</b>
Number of Chartered Projects			35
Board Approved Program Budget		\$	53,250,000
Remaining Unallocated Budget		\$	12,079,299

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020  
Table 8 - Information Technology Capital Program Status Report**

Project Number	Project Name	Status	Allocated Budget
IT16-03	Plant 2 Internet Connection	Active	\$ 50,000
IT16-05	Plant 2 Radio Repeater Upgrade	Closed	\$ 35,000
IT16-06	Network Equipment 2016-17	Closed	\$ 44,302
IT16-07	Server Replacement and Obsolescence	Closed	\$ 337,332
IT16-08	IT Security 2016-17	Active	\$ 162,000
IT16-09	iPACS Enhancements	Active	\$ 85,000
IT16-10	LIMS Compliance Improv Project	Closed	\$ 754,800
IT16-11	Business Continuity Plan	Active	\$ 140,000
IT17-01	VMWare	Active	\$ 800,000
IT17-02	Upgrade Active Directory Directory to 2016	Active	\$ 56,000
IT17-03	Upgrade ShoreTel System Server	Active	\$ 190,000
IT17-04	PCI Improvements	Closed	\$ 131,093
IT17-05	Conference Room Monitor Upgrade	Active	\$ 75,686
IT17-06	Printer Obsolescence	Active	\$ 350,000
IT17-07	Safety Management Suite	Active	\$ 106,000
IT17-08	Perimeter Physical Security Im	Closed	\$ 170,077
IT17-09	MYOCSD Redesign	Closed	\$ 170,077
IT17-10	Electronic Operator Round Form	Active	\$ 45,000
IT17-11	P2 Radio Repeater	Closed	\$ 170,077
IT17-12	Sever/Network Power Improvements	Active	\$ 90,000
IT17-13	Graphric Workstations for PAO	Closed	\$ 15,000
IT17-14	Specialized Application Programing & Support	Active	\$ 600,000
IT17-15	Data Storage Replac/Obsolescens	Closed	\$ 600,000
IT18-02	Fleet Management Information System	Active	\$ 250,000
IT18-03	Timecard Systems Upgrade	Active	\$ 150,000
IT18-04	Conference Rooms Audio System Replacement	Closed	\$ 90,000
IT18-05	Trusted System Document Management	Active	\$ 100,000
IT18-06	Server Replacement and Obsolescence FY18/19-19/20	Closed	\$ 900,000
IT18-07	Network Equipment FY18/19-19/20	Closed	\$ 850,000
IT18-09	Records Management Information System	Active	\$ 100,000
IT18-10	Board Services Management System	Closed	\$ 60,000
IT18-11	IT Security Budget 2018-2019	Closed	\$ 150,000
IT19-01	IT Safety VPP Systems (IT19-01)	Active	\$ 150,000
IT19-02	IT Enterprise Replication (IT19-02)	Active	\$ 150,000
IT19-03	IT HP Plotter (IT19-03)	Closed	\$ 150,000
IT19-04	IT HCI for ICS and ICS-DMZ (IT19-04)	Active	\$ 150,000
IT19-05	IT P1 & P2 Data Refresh (IT19-05)	Active	\$ 150,000
<b>Grand Total</b>			<b>\$ 8,577,444</b>
Number of Chartered Projects			37
Board Approved Program Budget		\$	10,000,000
Remaining Unallocated Budget		\$	1,422,556

**Capital Improvement Program Contract Performance Report  
for Quarter Ending 06/30/2020  
Table 9 - Operations & Maintenance Capital Program Status Report**

Project Number	Project Name	Status	Allocated Budget
SC16-01	Maint. Storage Area Tool Cage	Active	\$ 12,000
SC17-01	CENGEN #1 Elevator Rehab	Active	\$ 12,000
SC17-02	P1 CenGen Plant Water Piping Rehabilitation	Active	\$ 250,000
SC17-03	CenGen Oil Filter Platform	Active	\$ 260,000
SC17-04	P1 CenGen 12KV Circuit Breaker Replacement	Closed	\$ 220,000
SC17-05	Hidrostal Pump - TEFC Close Coupled Motor #2 (Pump for SALS)	Active	\$ 261,260
SC17-06	P1 Lab UPS System Replacement	Active	\$ 290,294
SC18-01	P1 Primary Clarifier Fall Protection Improvements	Active	\$ 50,000
SC18-02	Joint Cen Gen Oil Centrifuge Heater & Controls Rehabilitation (MP-18)	Active	\$ 120,000
SC18-03	P1 SALS Main Duty Pump & Motor and Installation - Remaining 2 (MP-524)	Active	\$ 500,000
SC18-04	Edinger UPS Replacement (MP-444)	Active	\$ 15,000
SC18-05	P1 Laboratory HVAC Boiler Burner Replacement At Plant No.1	Active	\$ 400,461
SC18-06	Pump Station Bypass Parts - Procurement (MP-426)	Active	\$ 500,000
SC18-08	MacArthur Pump Station - FM Valve Replacement	Active	\$ 55,109
SC18-09	Admin Bldg UPS System Replacement	Active	\$ 185,000
SC18-10	P2 South Scrubber Complex Bleach Pump Turndown (MP-420)	Active	\$ -
SC18-11	Lido PS Camlock Con Panel Inst (SC18-11)	Active	\$ -
SC19-02	Truck Loading-Conveyors 3&6 (SC19-02)	Active	\$ 359,176
SC19-03	Return Activated Sludge Pump Station Elevator Rehabilitation at Plant No. 2	Active	\$ 890,000
SC19-04	Standby Generator Diesel Day Tank Improvements at Plant No. 1	Active	\$ 250,000
SC19-06	EPSA Standby Power Generator Control Upgrades at Plant No. 2	Active	\$ 1,251,500
<b>Grand Total</b>			<b>\$ 5,881,800</b>
Number of Chartered Projects			21
Board Approved Program Budget			\$ 15,622,000
Remaining Unallocated Budget			\$ 9,740,200





**ORANGE COUNTY SANITATION DISTRICT**  
**Capital Improvement Program**  
**Contract Performance Report**  
 For the period ending June 30, 2020

**PART 4 – SUPPLEMENTAL ENGINEERING SERVICES CONTRACT**

In May 2016, the Sanitation District Board of Directors approved a \$41 million professional services agreement with Jacobs Project Management Co. to provide supplemental engineering and support staff services for a four-year term with the option of three one-year renewals. The benefits of using a supplemental engineering services contract, as opposed to hiring full-time staff or limited-term employees, include rapid mobilization of highly skilled/technical staff, flexibility to change the mix of staff positions on an immediate and as-needed basis, the ability to reduce staff as workloads decrease, access to technical experts to support special tasks, and access to staff with wastewater project experience.

A status table for the supplemental engineering services contract summary is attached under Table 10, and the supplemental engineering services labor summary can be found under Table 11.

**Table 10 – Supplemental Engineering Services Contract Status**

	<b>Total Fees</b>	<b>Time</b>
Contract	\$41,000,000	86 months <sup>(1)</sup>
Actuals to Date	\$21,232,459 52%	50 months 58%
Remaining	\$19,767,541 48%	36 months 42%

<sup>(1)</sup> Assuming three 1-year extensions

**Table 11 - Supplemental Engineering Services Labor Summary**

	<b>This Quarter</b>	<b>Inception to Date</b>
Labor Hours	9,638	158,698
Full Time Equivalent	21.4	21.2
Labor Costs (no expenses)	\$1,266,770	\$20,795,266
Average Hourly Rate	\$127	\$131
