


PCSA Effort Impacts



- Extended contract duration due to construction delays
- Higher number of resubmittals
- Request for Information (RFI) coordination more effort than anticipated
- Duplicate coordination effort with second Furniture, Fixtures, and Equipment (FFE) vendor
- Unexpected items requiring consultant support:
 - Distributed Antenna System (DAS) requirement
 - SCE street light metering requirements
 - Stormwater system redesign

3

Distributed Antenna System (DAS) ADAS is normally required for high-rise buildings. Energy efficiency glass impact police and fire communication signal requiring a DAS.

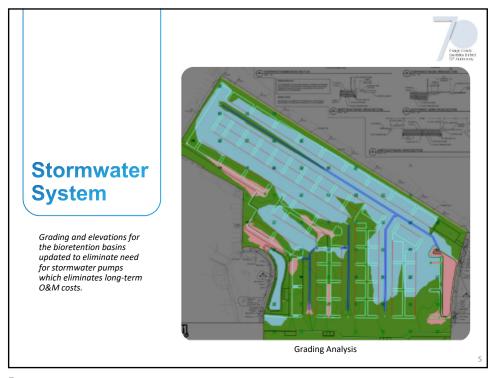

5

PCSA Effort Impacts



Projected Amount to Complete Project	
Additional Construction Technical Support	\$203,000
Remaining Contingency	(\$75,000)
Additional Budget Required (2.6%)	\$128,000

Requested Budget (3%) = \$147,000

6

Recommendation



Recommend to the Board of Directors to:

Approve a contingency increase of \$147,000 (3%) to the Professional Construction Services Agreement with HDR Engineering, Inc. for Headquarters Complex at Plant No. 1, Project No. P1-128A, for a total contingency of \$735,000 (15%) and a total contract amount not to exceed \$5,635,000.

7

7

